




UNDER CONSTRUCTION

MAPS – Manistee Area Public Schools – 550 Maple Street




Current Major Activities/Tasks

- Overhead Duct work being installed upper level
- Installing supplemental steel for roof top unit ductwork
- Electricians cutting caping and making safe
- Demo of masonry walls main level
- Abatement of main level girls locker room complete – passed clearance
- Abatement at main office complete – awaiting clearance

Continuing Major Activities/Tasks

- MEP overhead rough ins
- Demo/abatement
- Supplemental steel

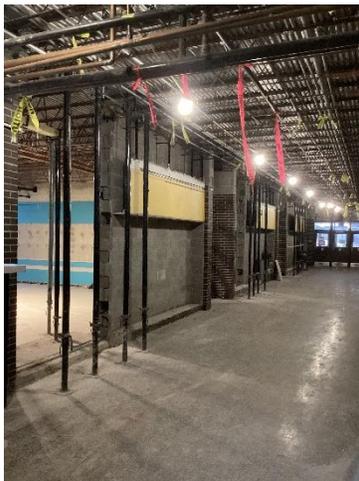

Main Level Wall Demolition for Future Bathrooms



Asbestos Containment of Office



Aux. Gym RTU Reinforcing



Abatement of Ceiling Girls Locker Room
